


CENTRAL FLORIDA EXPRESSWAY AUTHORITY

Wekiva Parkway
Construction Update

WEKIVA PARKWAY

3 Projects Under Construction

- 250 workers on the project on any given day
- 18% Complete
- \$182,394,748.99 Under Contract

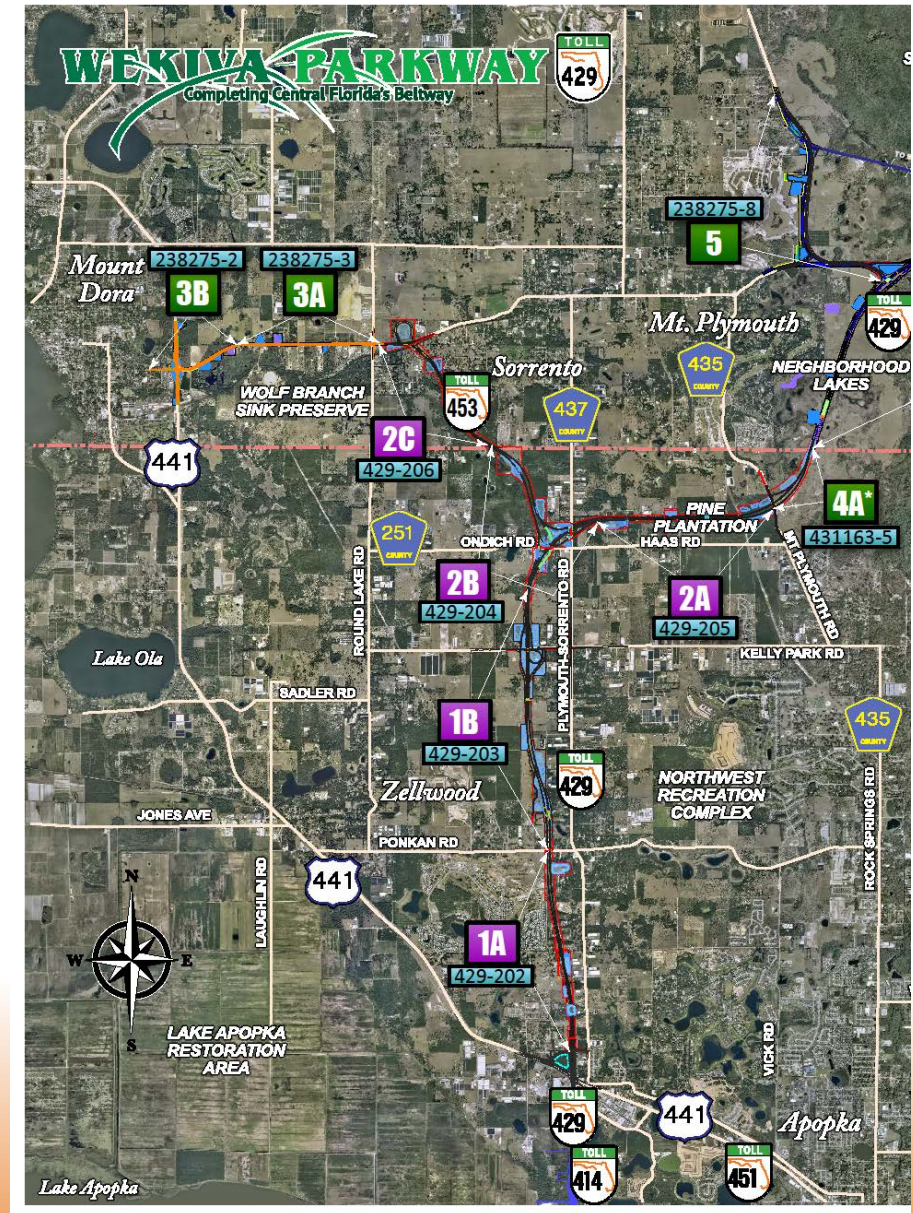



Section 429-202 (1A)

From North of US 441 to North of Ponkan Rd.

Started: June 8, 2015

Contractor: Prince Construction

Contract : \$56,152,429.00

Time: 660 Calendar Days

% Complete: 29%

Anticipated Finish: April 2017





Section 429-203 (1B)

From North of Ponkan Rd. to North of a
New Kelly Park Road Interchange

Started: August 3, 2015
Contractor: Superior Construction
Contract: \$46,617,017.39
Time: 600 Calendar Days
% Complete: 32%
Anticipated Finish: April 2017





Section 429-204 (2B)

Systems Interchange extending Wekiva Parkway (SR 429)
northeast toward Sanford and SR 453 toward Mount Dora

Started: January 4, 2016

Contractor: Southland Construction


Contract: \$79,625,302.60

Time: 730 calendar days

% Complete: 2%

Anticipated Finish: January 2018



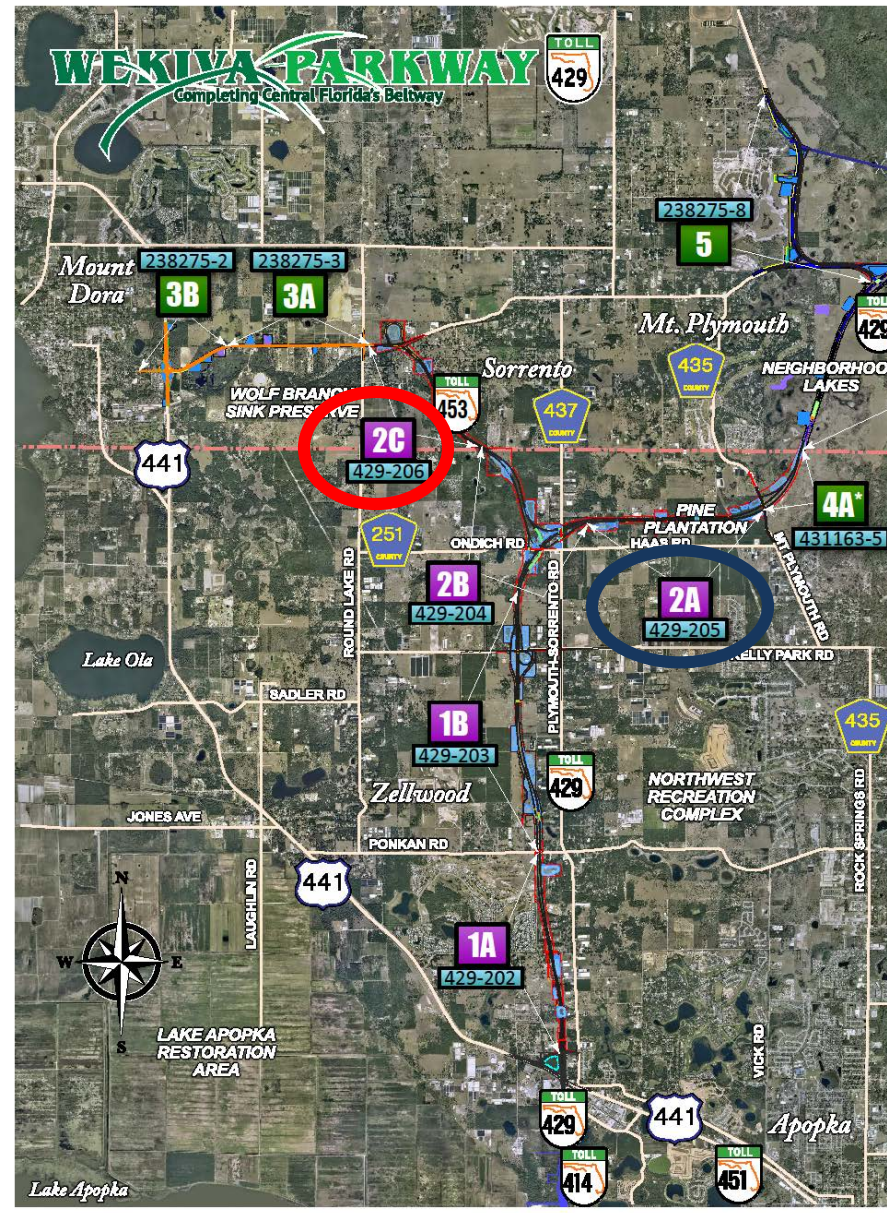



Wekiva Parkway

Section 429-206 (2C)

Bid Information:

- Bids received February 23, 2016
- 12 bids received
- Engineers' Estimate: \$57,486,618.81
- High Bid: \$58,814,677.09
- Low Bid: \$49,482,671.93 (GLF Construction)
- Anticipated NTP date: May 1, 2016
- Construction duration: 600 calendar days
- Anticipated open to traffic date: January 2018

Contract Approval

Recommended Motion:

Approval of the award of Section 206/Wekiva Parkway construction contract to GLF Construction, Inc. in the amount of \$49,482,671.93.
