




CENTRAL FLORIDA EXPRESSWAY AUTHORITY

WEKIVA PARKWAY CONSTRUCTION UPDATE

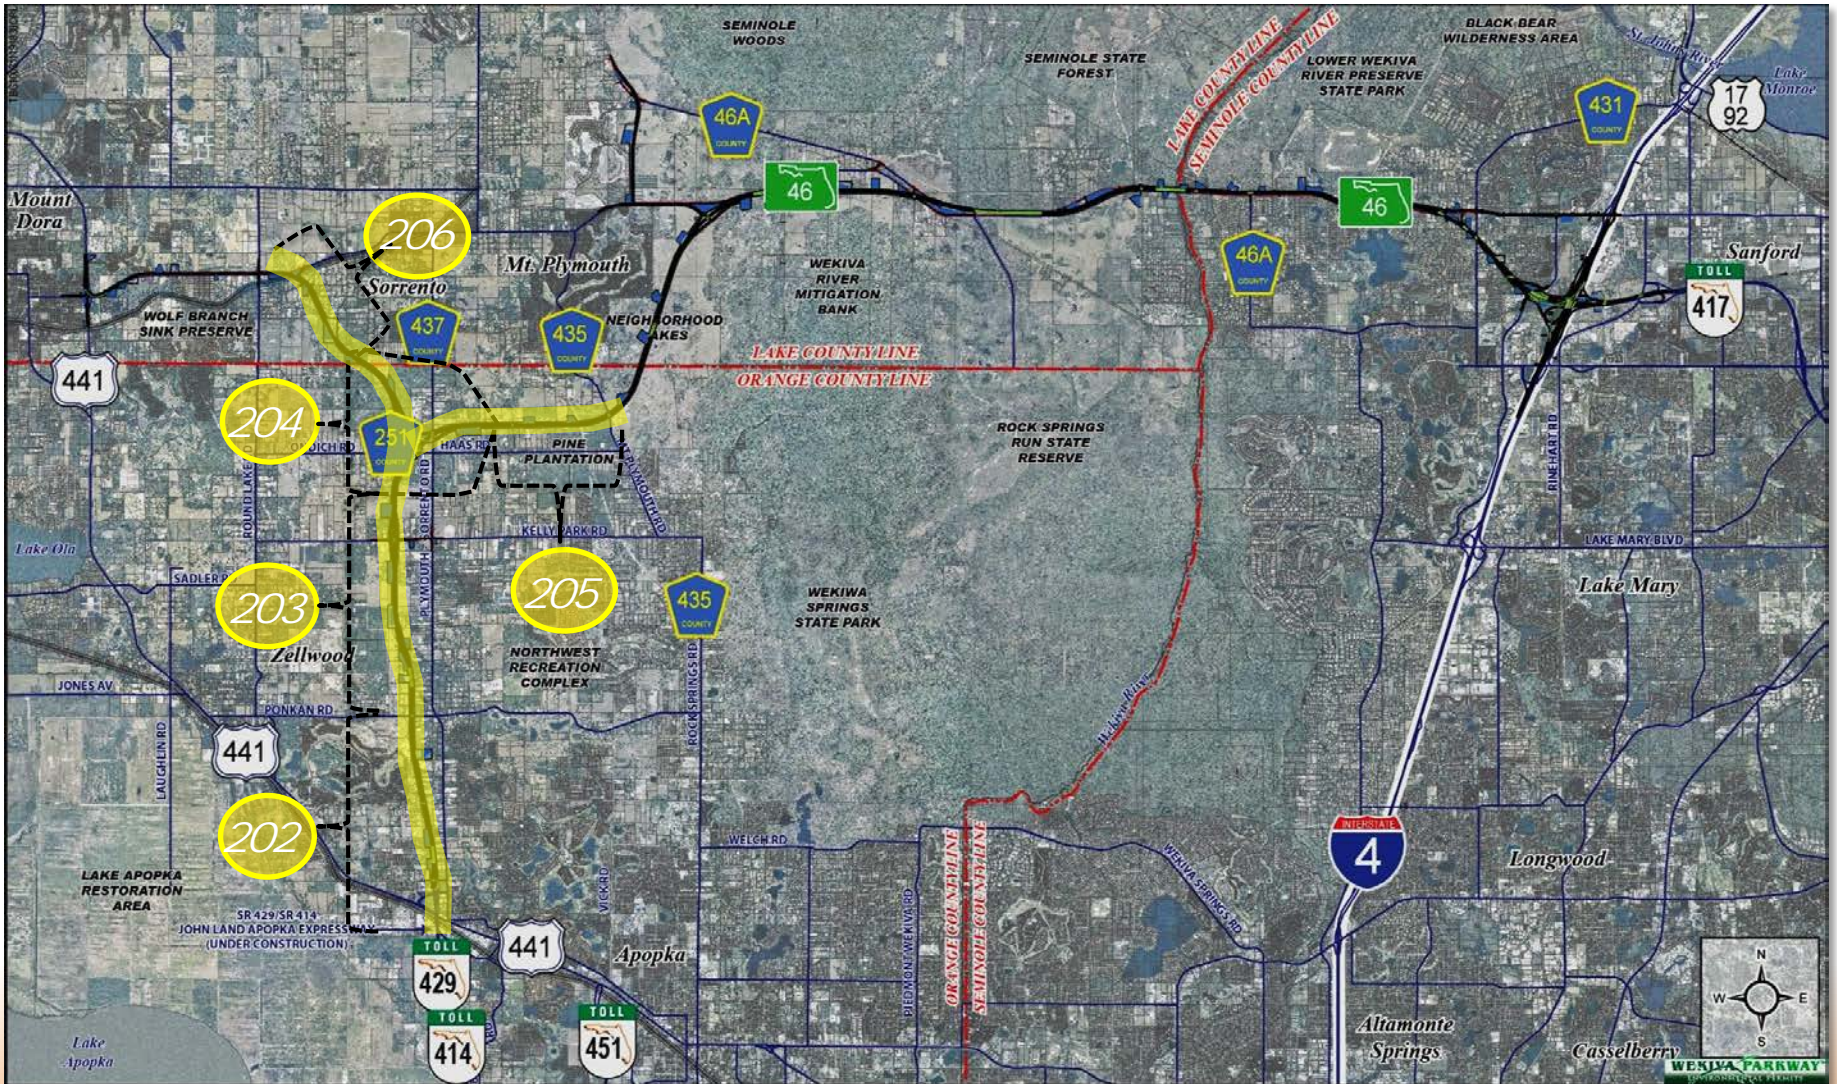


CENTRAL FLORIDA EXPRESSWAY AUTHORITY

WEKIVA PARKWAY

5 projects under construction

- ~465 construction workers on the project on any given day
- \$271,643,087.52 under contract
- \$119,645,177.30 earned thru 10/25/16
- 44% complete

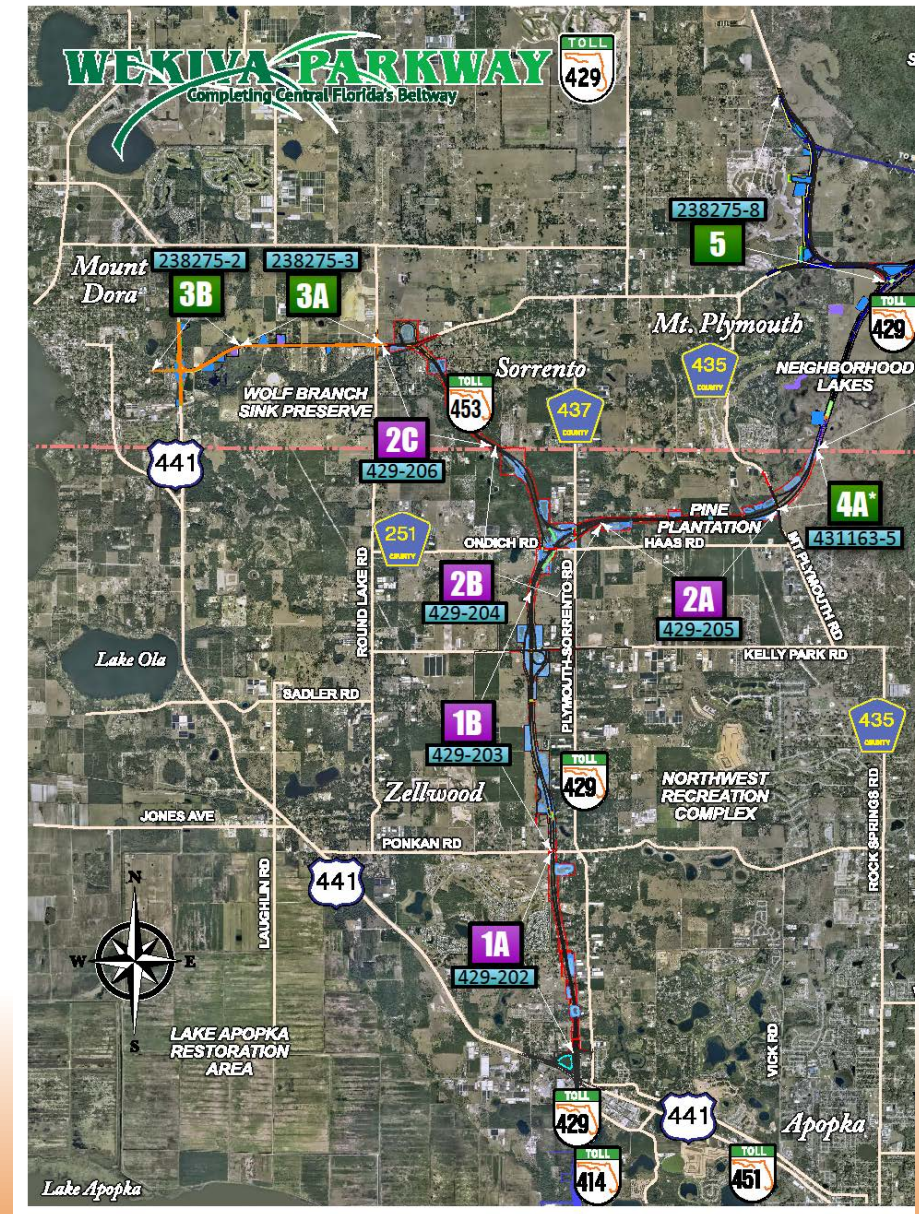



Section 429-202 (1A)

From North of US 441 to North of Ponkan Rd.

Started: June 8, 2015

Contractor:
Prince Construction

Contract: \$56,325,741.99

Earned: \$38,325,919.80

Time: 679 calendar days

Percent Complete: 68%











Section 429-203 (1B)

From North of Ponkan Rd. to North of a New Kelly Park Road Interchange

Started: August 3, 2015

Contractor:

Superior Construction

Contract: \$46,499,984.12

Earned: \$35,795,197.65

Time: 600 calendar days

Percent Complete: 77%






CENTRAL FLORIDA EXPRESSWAY AUTHORITY



CENTRAL FLORIDA EXPRESSWAY AUTHORITY

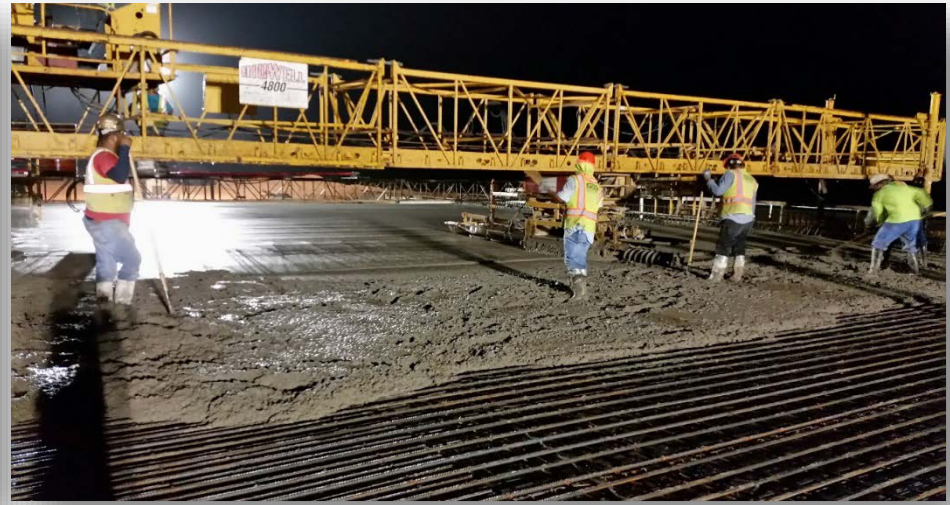



Section 429-204 (2B)

Systems Interchange extending Wekiva Parkway (SR 429) northeast toward Sanford and SR 453 toward Mount Dora

Started: January 4, 2016

Contractor:

Southland Construction

Contract: \$80,684,689.48

Earned: \$28,037,936.96

Time: 730 calendar days

Percent Complete: 35%





CENTRAL FLORIDA EXPRESSWAY AUTHORITY







Section 429-205 (2A)

Wekiva Parkway (SR 429) from the Systems Interchange east to FDOT's completed Section 4A at CR 435

Started: August 1, 2016

Contractor:

Superior Construction

Contract: \$38,650,000.00

Earned: \$4,422,342.88

Time: 570 calendar days

Percent Complete: 11%





CENTRAL FLORIDA EXPRESSWAY AUTHORITY





Section 429-206 (2C)

North-West leg of the Wekiva Parkway (SR 453) extending from the Lake County Line to SR 46 toward Mount Dora

Started: May 2, 2016

Contractor: GLF Construction

Contract: \$49,482,671.93

Earned: \$13,063,780.01

Time: 600 calendar days

Percent Complete: 26%







When Complete, we will have:

- Excavated ~3,597,000 Cubic Yards of Earth (18 Large Cruise Ships)
- Built ~8,391,000 Cubic Yards of Embankment (42 Large Cruise Ships)
- Built ~92 Lane Miles of Roadway
- Driven ~ 40 Miles of Foundation Piles
- Built ~ 7.5 Lane Miles of New Bridges
- Planted ~ 440,000 Square Yards of Seed & Mulch (83 Football Fields)
- Placed ~ 2,280,000 Square Yards of Sod (428 Football Fields)



WEKIVA PARKWAY CCEI & COMPLIANCE TEAMS

- 429-202: **RK&K**, CDM Smith, RS&H, PICS (DBE), PSI, URS, Terracon, Elipsis (DBE) AMEC, Mehta (DBE)
- 429-203: **GAI**, DRMP, PI Consulting (DBE), Page One, Ardaman, FGE, GPI, Mehta (DBE)
- 429-204: **A2** (DBE), Figg, RK&K, DRMP, GCI (DBE), Mehta (DBE), Gannett Fleming & Page One (DBE)
- 429-205: **KCCS**, Elipsis (DBE), GRL, PICS (DBE), Page One (DBE) & Echezabal (DBE)
- 429-206: **Jacobs**, Metric, FGE, Aerial Innovations, Ardaman, Elipsis (DBE) & Mehta (DBE)
- Corridor-Wide Compliance: **MTN Resources**



WEKIVA PARKWAY OPENING PLAN

- Mid 2017: Open Wekiva Parkway from Connector Road to Kelly Park Road (Projects 429-202 & 429-203)
- Early 2018: Open remainder of CFX Wekiva Projects (429-204, 429-205 & 429-206)
