




A Regional Transportation Solution



**Central Florida Expressway Authority
Board Update
April 9, 2015**



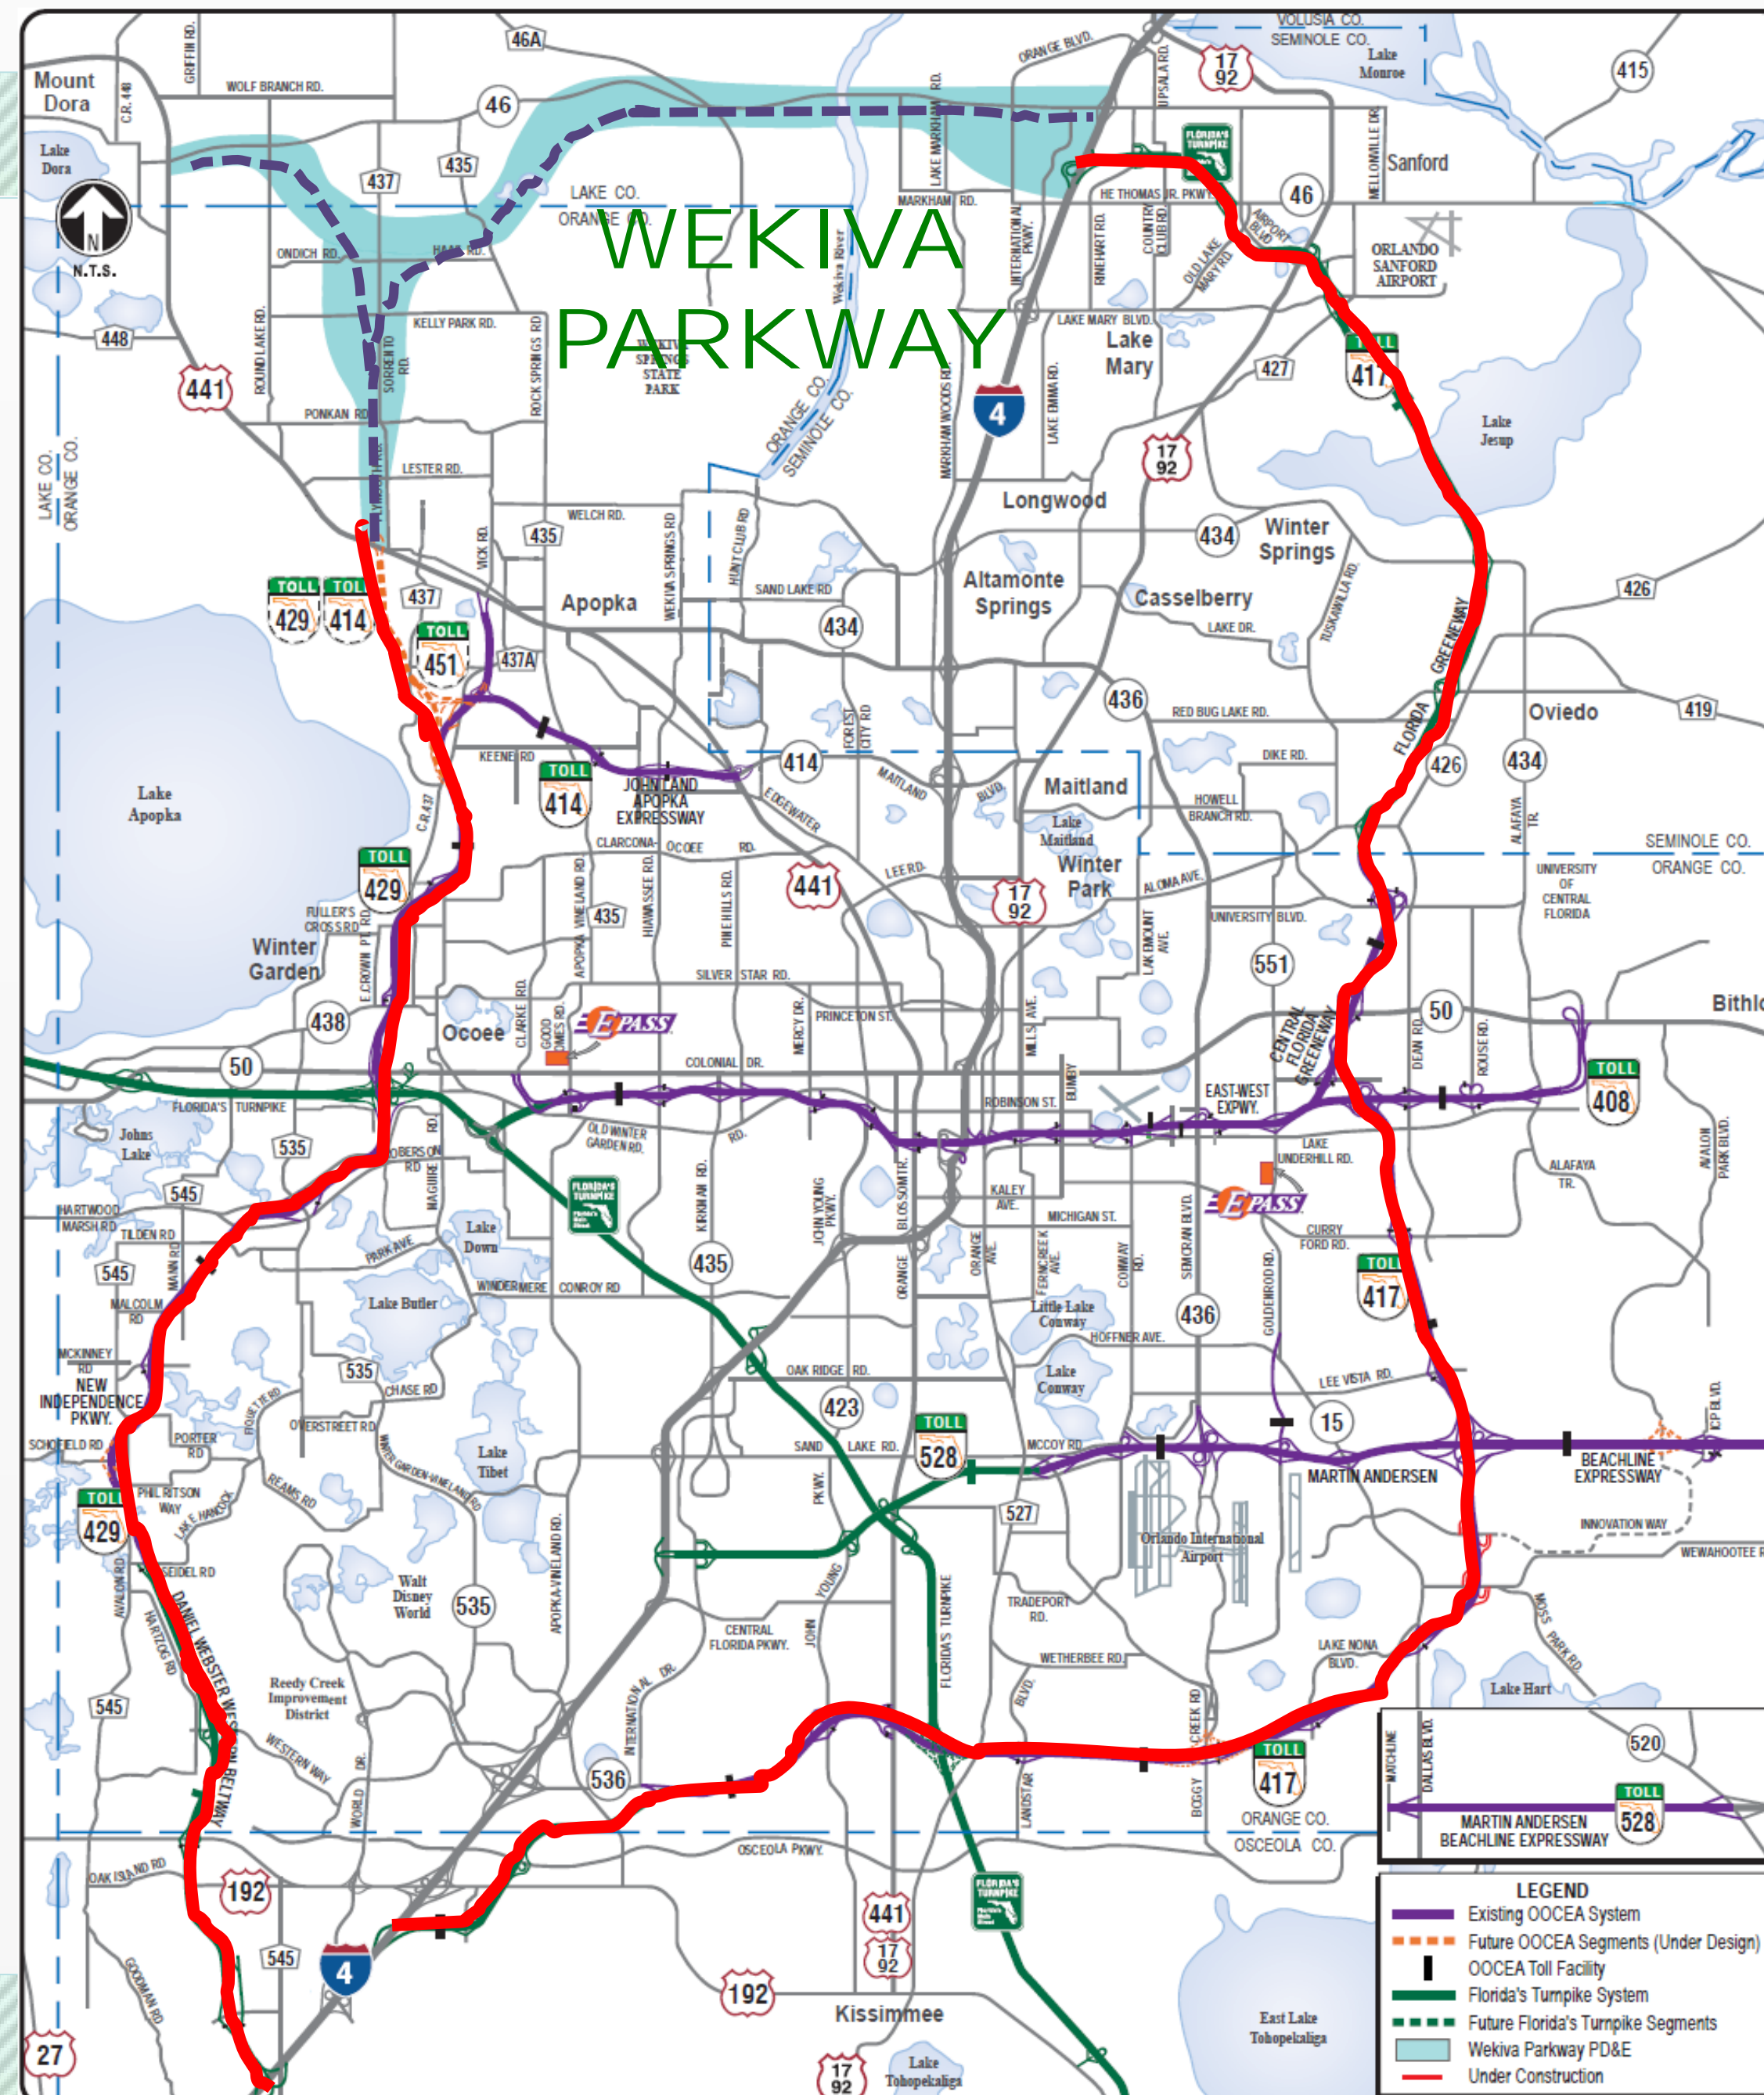


Project Highlights

- All Electronic Tolling
- Landmark Environmental Considerations
- 10-Mile Multi-Use Trail



Aesthetics Plans

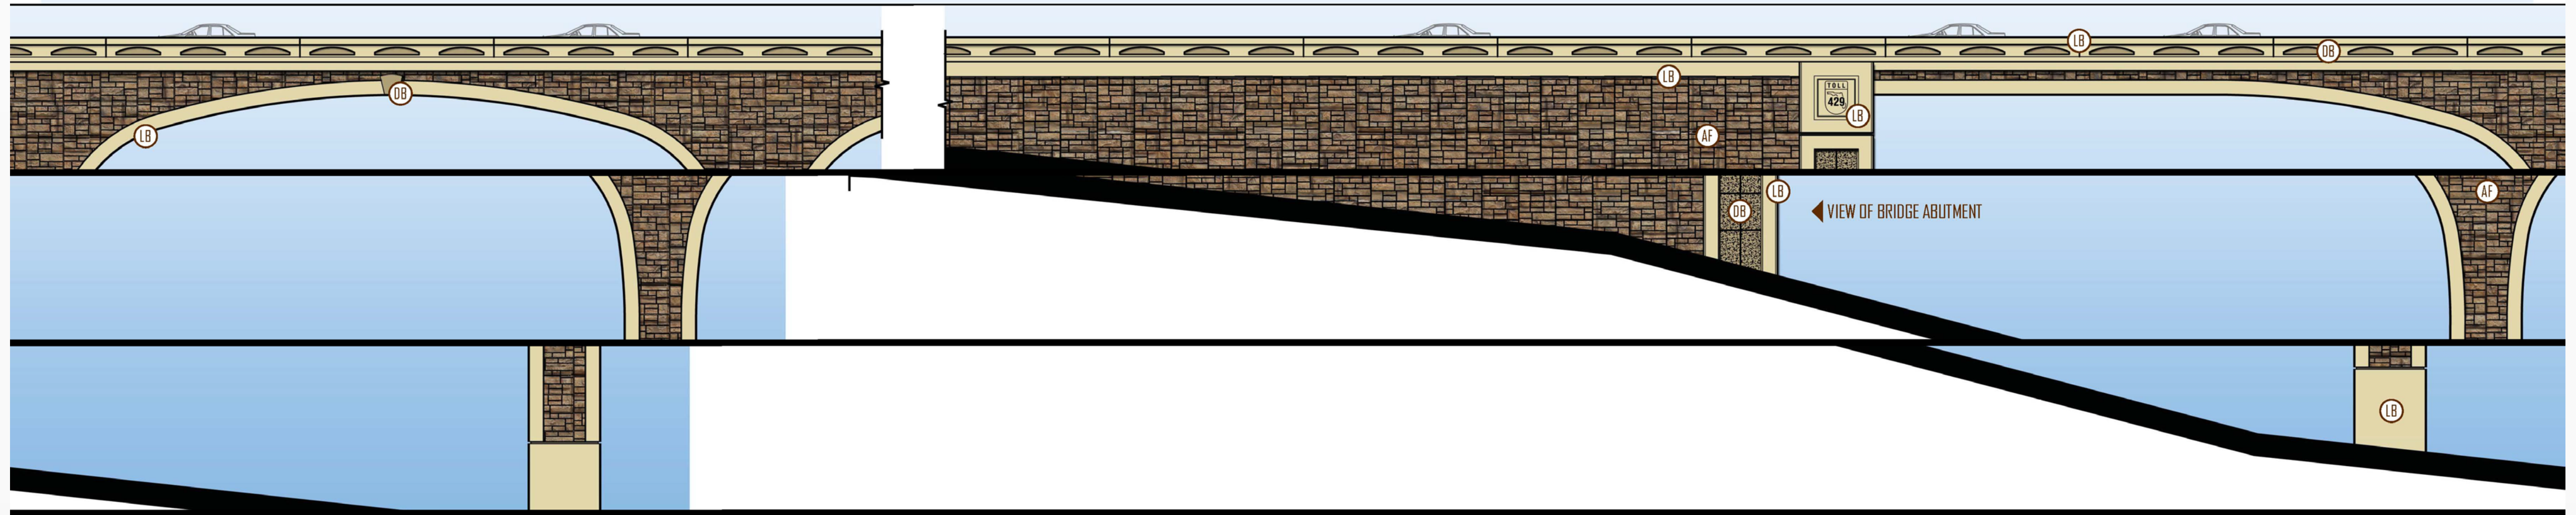




Regional Project

By the Numbers:


- 3 Agencies
- 14 Project Sections
- 3 Counties, 3 Cities, State & Federal Agencies
- Wekiva River Basin Area Task Force, Coordinating Committee & Wekiva River Basin Commission
- PD&E Study:
 - ✓ 30,000+ Property Owners
 - ✓ 400+ Community & Agency Stakeholder Meetings
 - ✓ 9 Public Meetings & Hearings Drawing 3,600 People



Public Outreach Program



Elected Officials' Briefings
Community Presentations
Public Meetings
Youth Outreach Program
Stakeholder Meetings
Wekiva River Bridge Charrettes
Special Events
Media Events
Interactive Website
Social Media

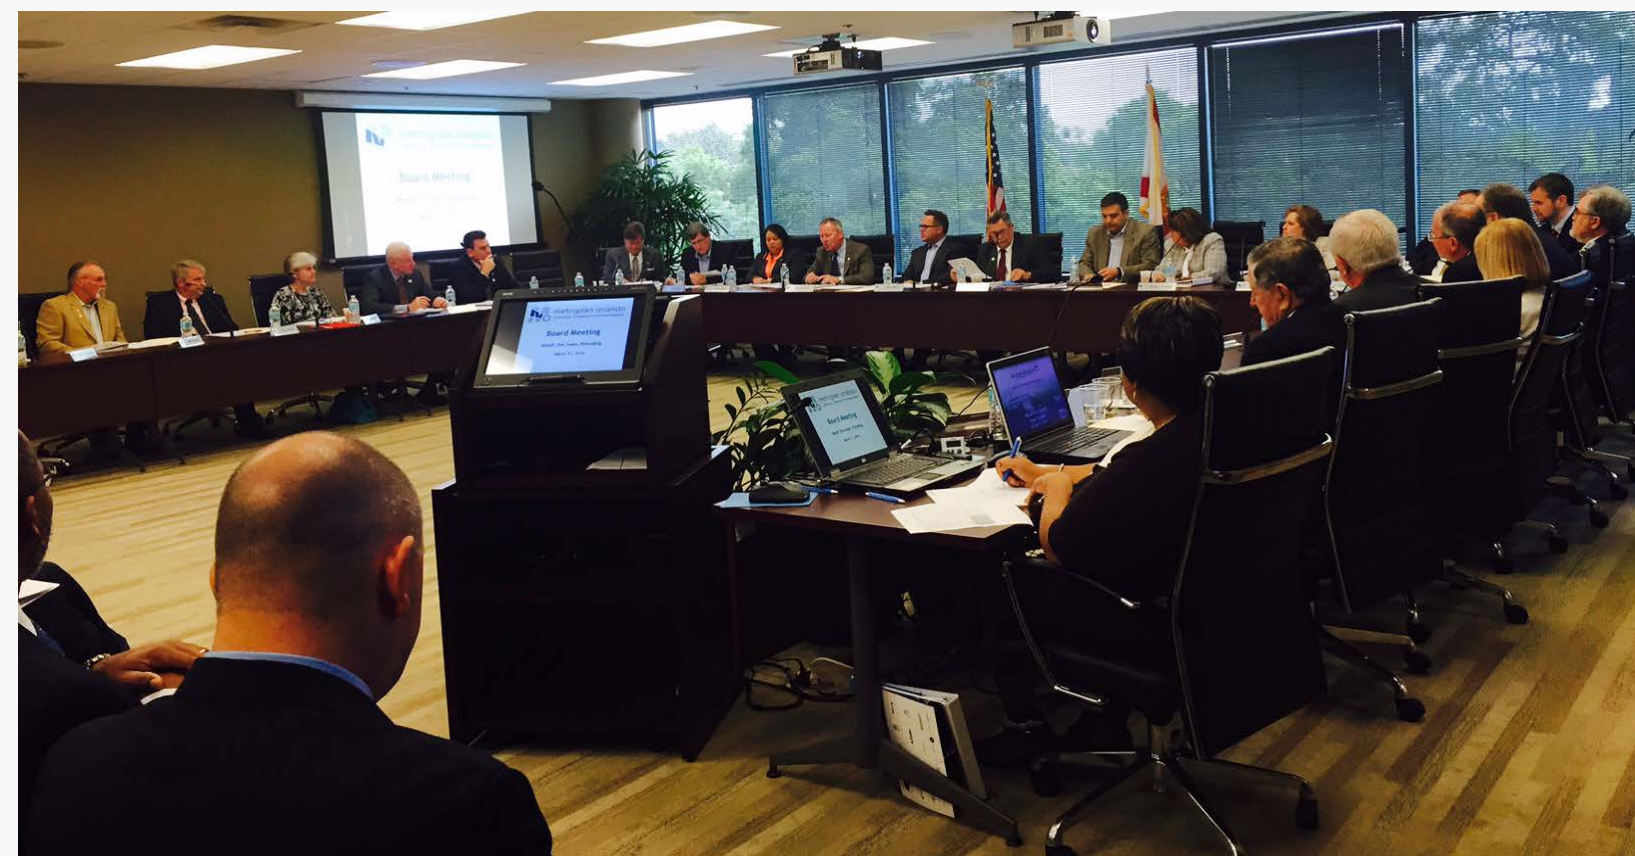

Youth Outreach Program

Leesburg HS Engineering Student Tour – March 25, 2015

Leesburg HS & District Magnet Program Staff – Jan. 15, 2015

Round Lake ES PTO / SAC – Dec. 18, 2014


Apopka ES Teach In – Nov. 19, 2014

Round Lake ES Principal Bartberger & Staff – Nov. 4, 2014

Apopka ES School Assist. Principal Vazquez – Oct. 2, 2014


Seminole County Natural Lands Eco Camp – July 28, 2014

Seminole 4-H Clover Kids Club – May 5, 2014




CFX Sections 1A & 1B Update

- ✓ Design Complete
- ✓ Pre-Construction Community Open House
(Sept. 25, 2014 – 130 Attendees)
- ✓ CEI's Selected: RK&K, GAI
- ✓ Section 1A Construction Start: June 1, 2015
(Contractor: Prince)
- ✓ Section 1B Construction Start: Aug. 1, 2015
(Contractor – Advertised April 5)

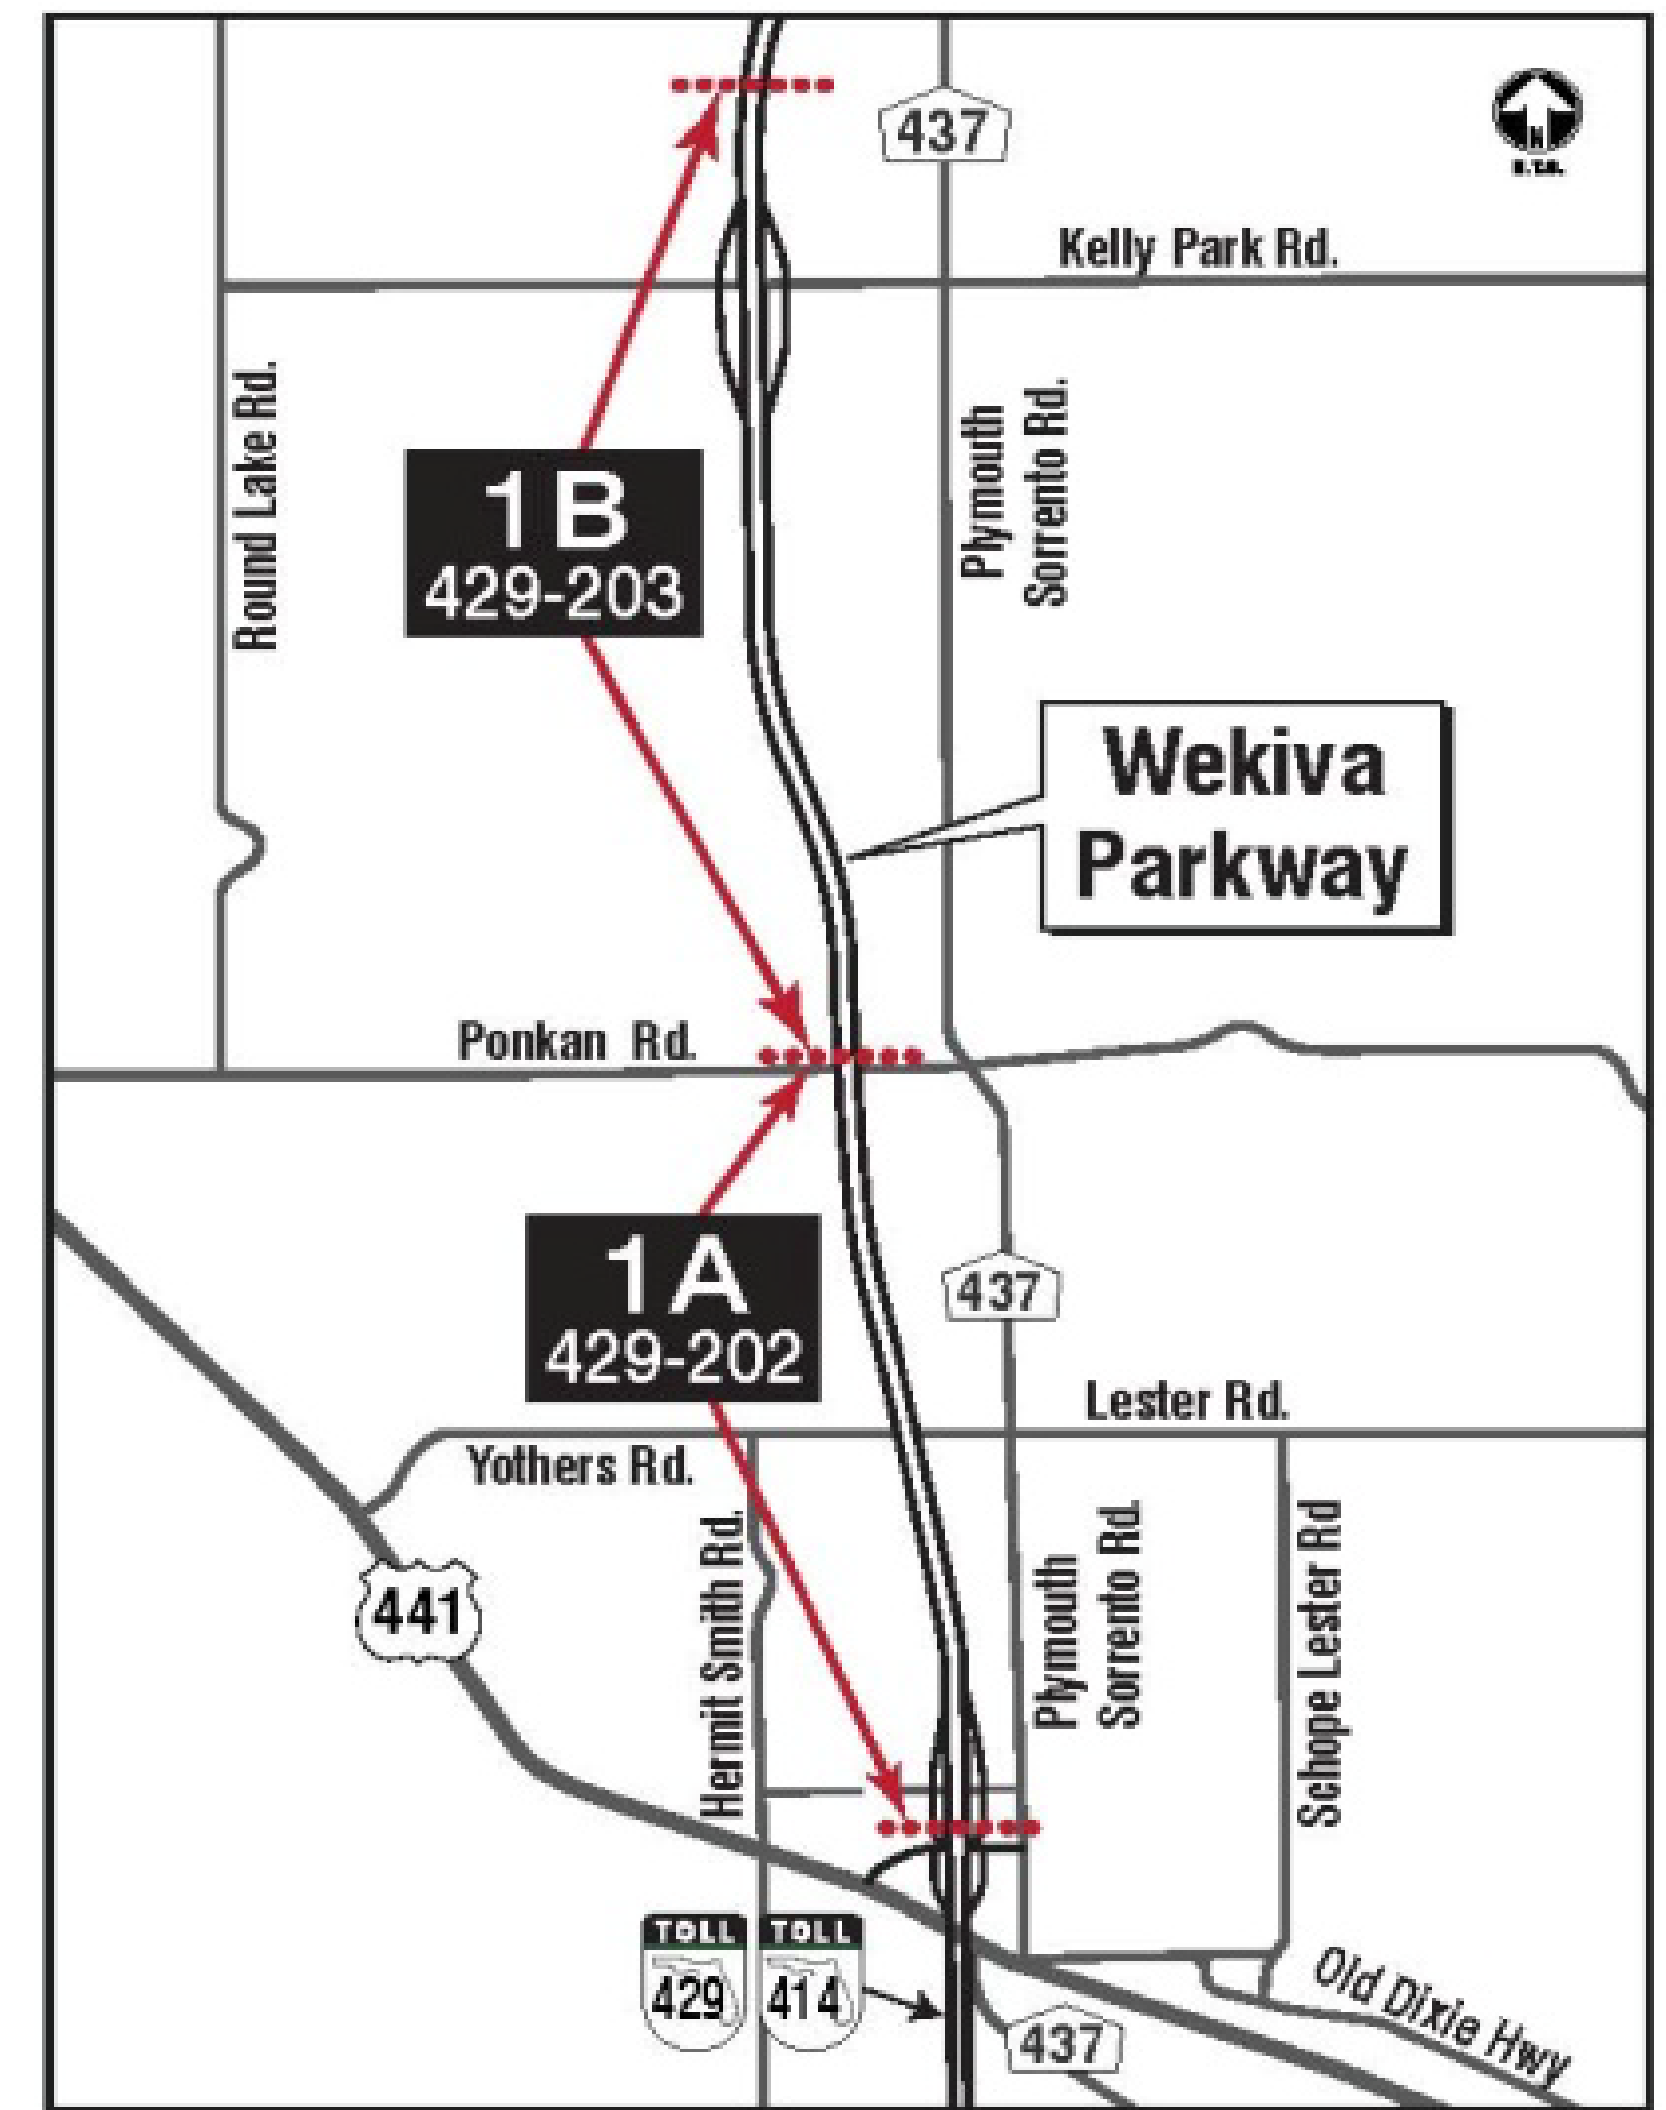

CFX Sections 2A, 2B & 2C Update

- ✓ Design Complete: 2015
- ✓ Section 2B:
 - ✓ CEI Procurement: March 29
 - ✓ Contractor Ad: September
 - ✓ Construction Start: Jan. 1, 2016
- ✓ Section 2C
 - ✓ CEI Procurement: July-Aug. 2015
 - ✓ Contractor Ad: Dec. 2015
 - ✓ Construction Start: Apr. 1, 2016
- ✓ Section 2A
 - ✓ CEI Procurement: July-Aug. 2015
 - ✓ Contractor Ad: Dec. 2015
 - ✓ Construction Start: May 1, 2016

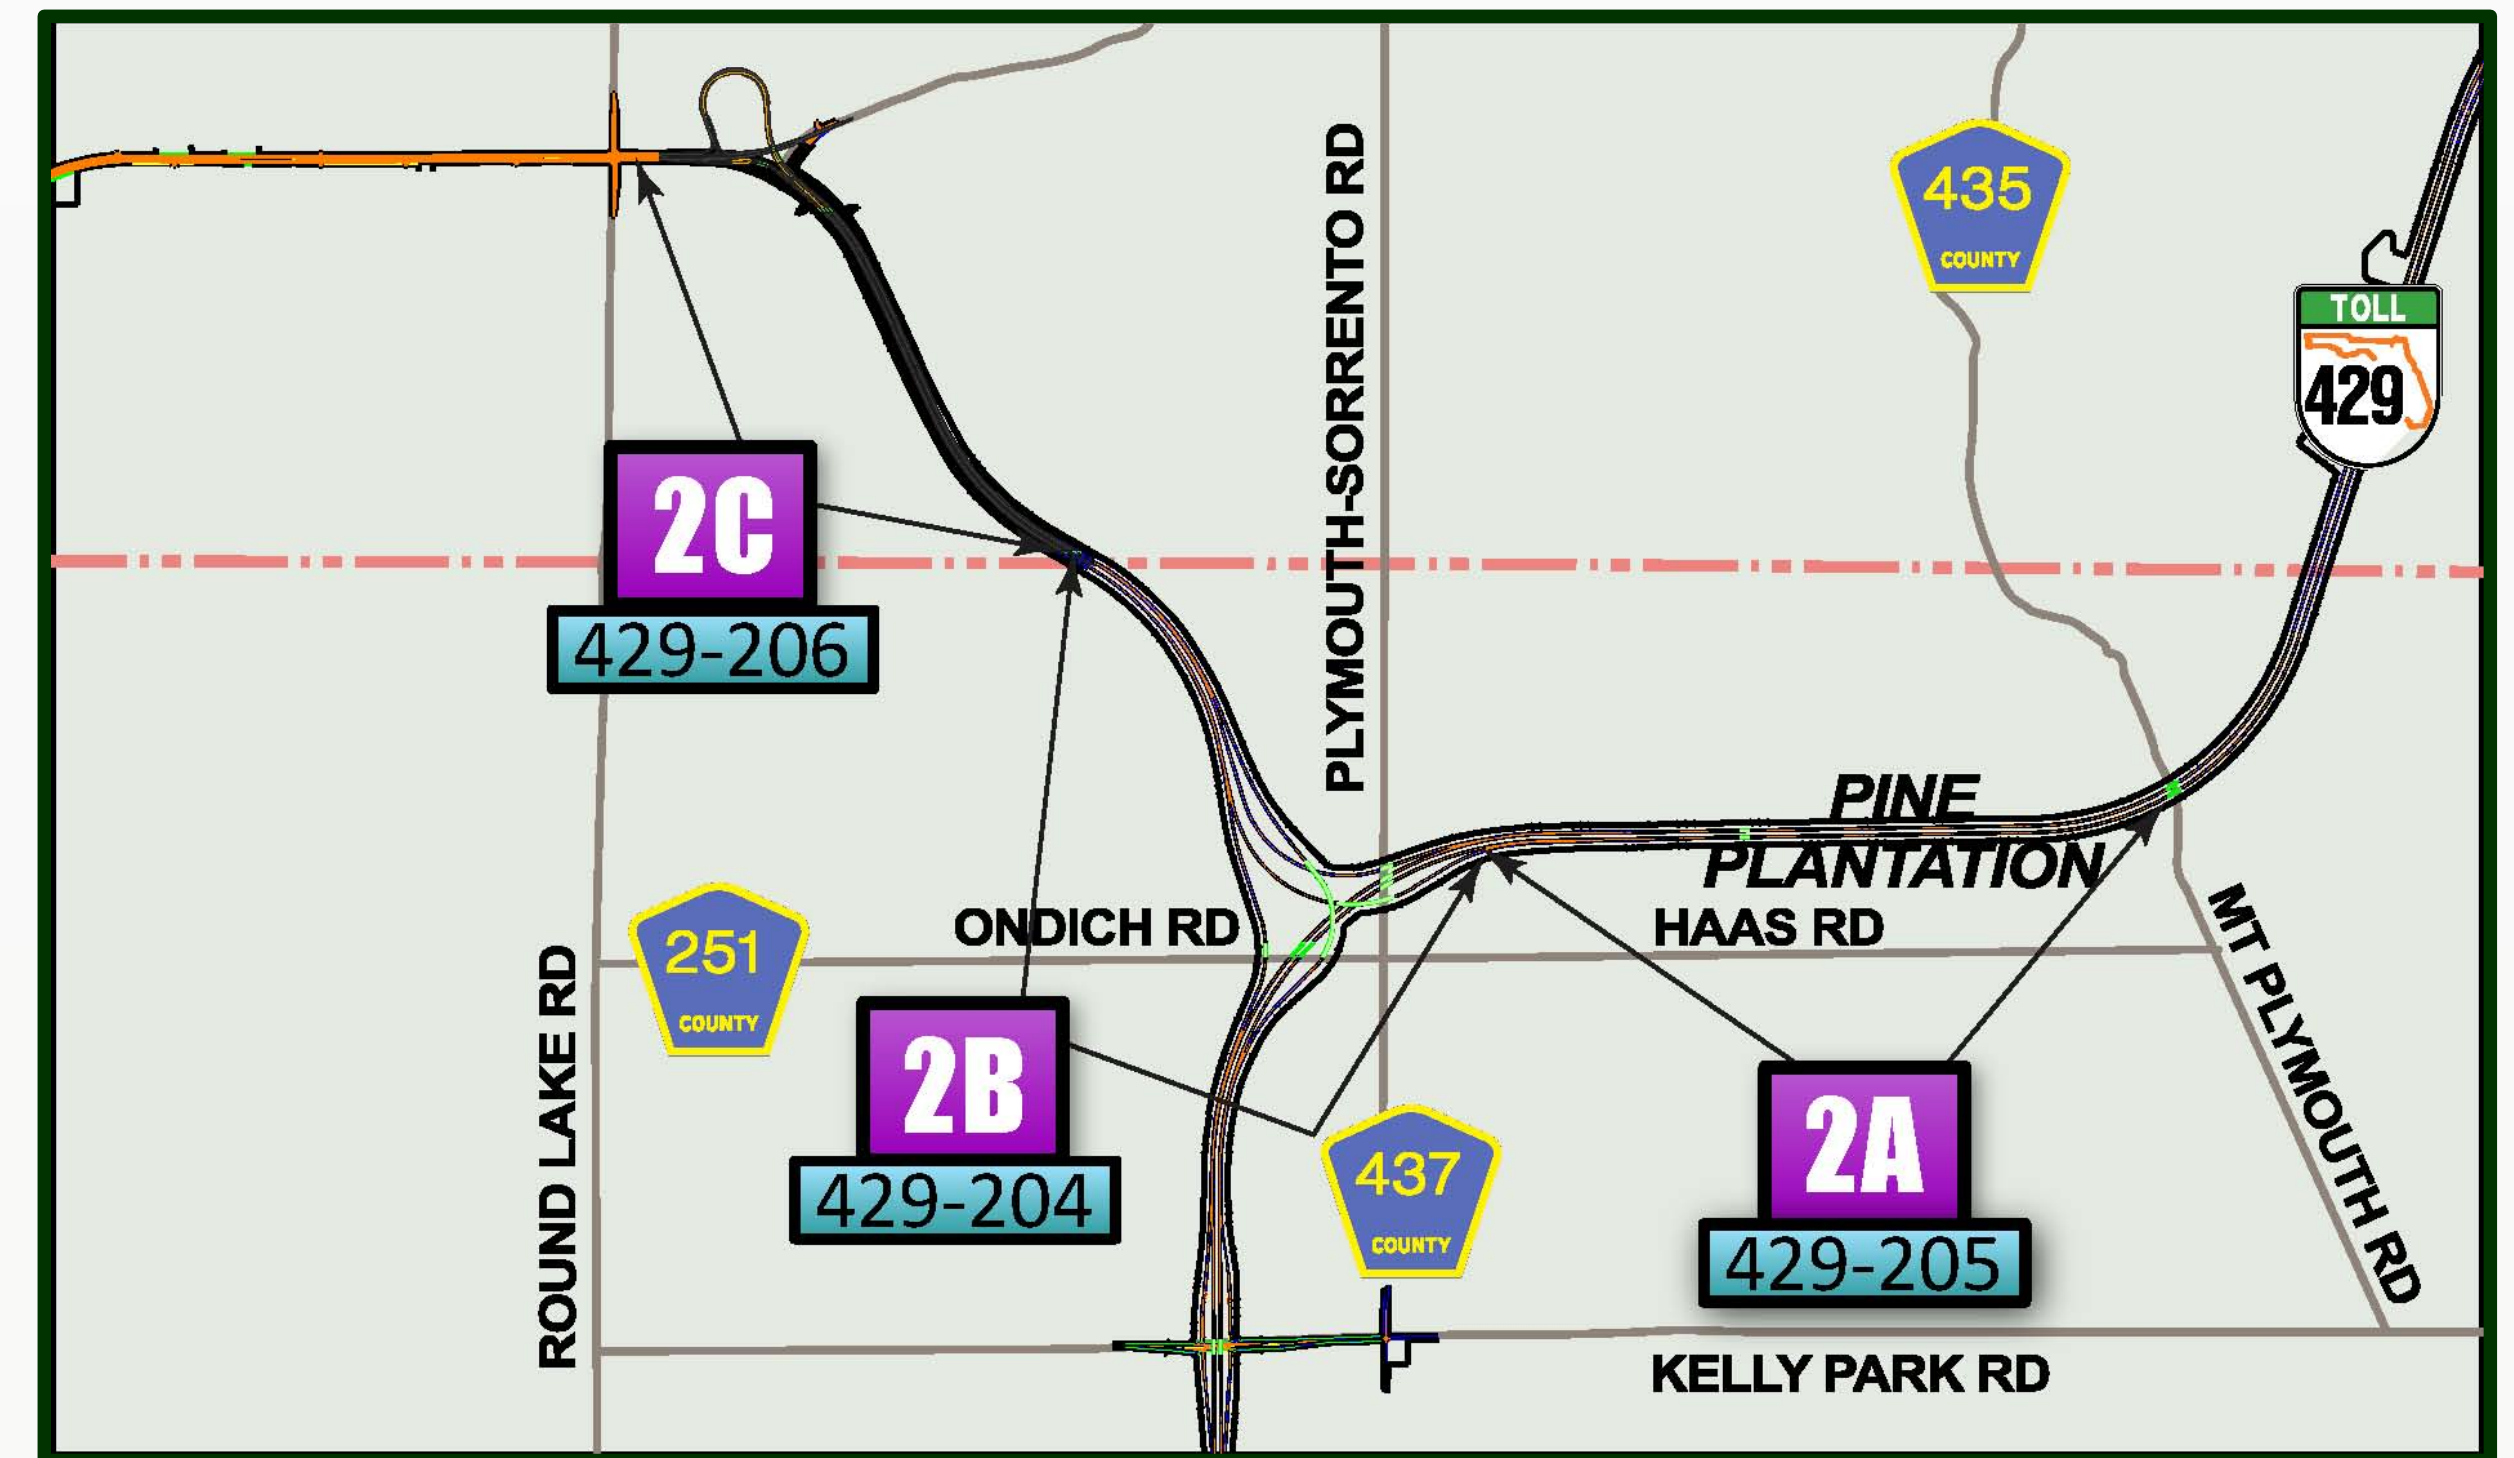


- ✓ Pre-Construction Public Meeting:
September 2015

FDOT Sections 4A & 4B Update




Flagging Operations SR 46
Completion: Summer 2015
Future Trail

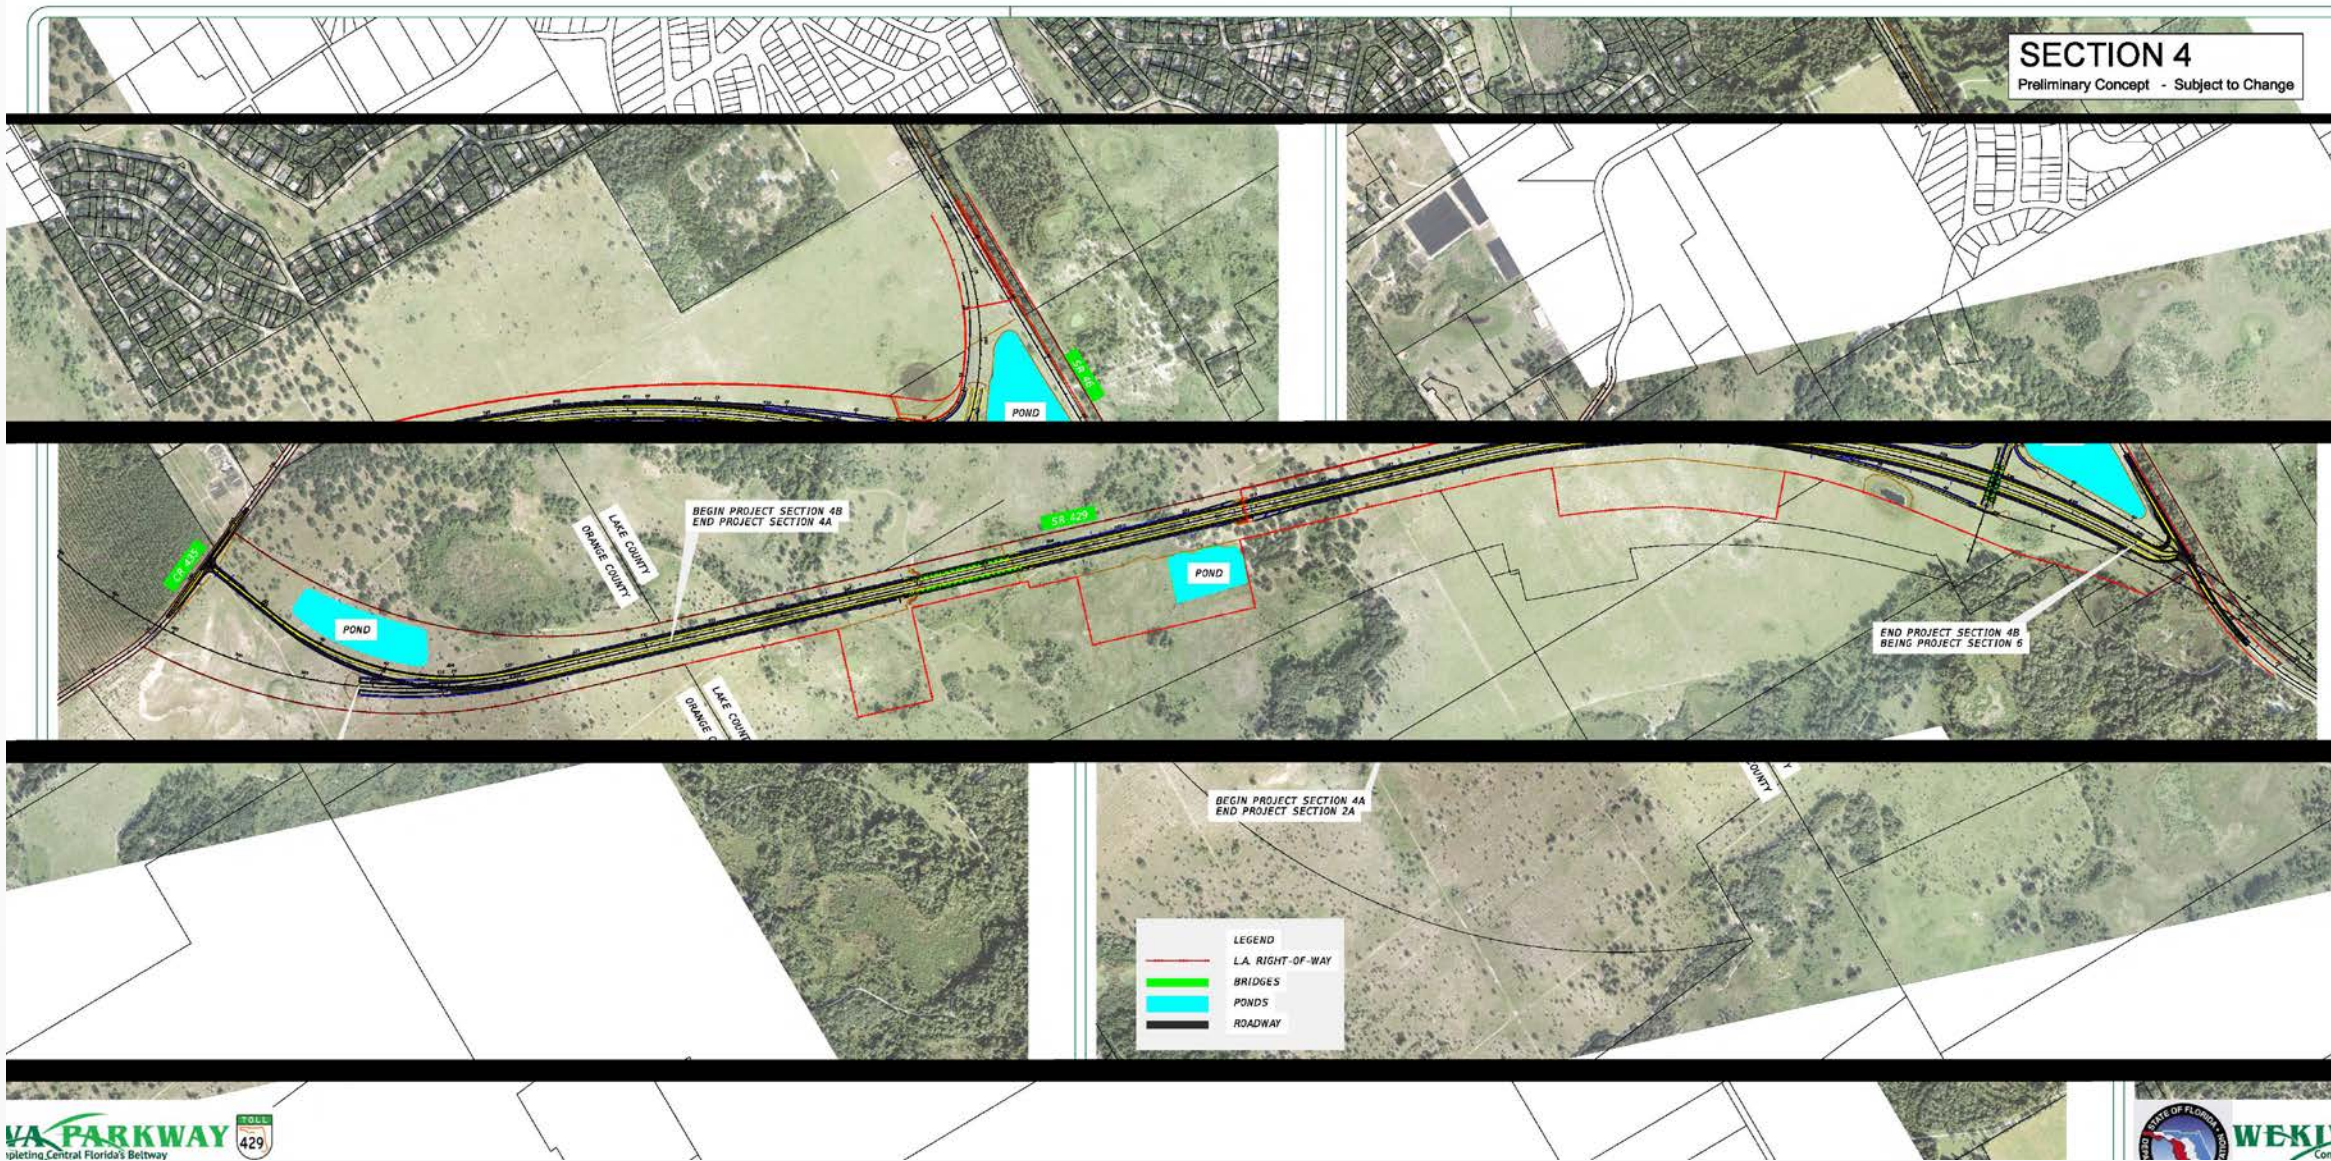

WEKIWA PARKWAY

Completing Central Florida's Beltway

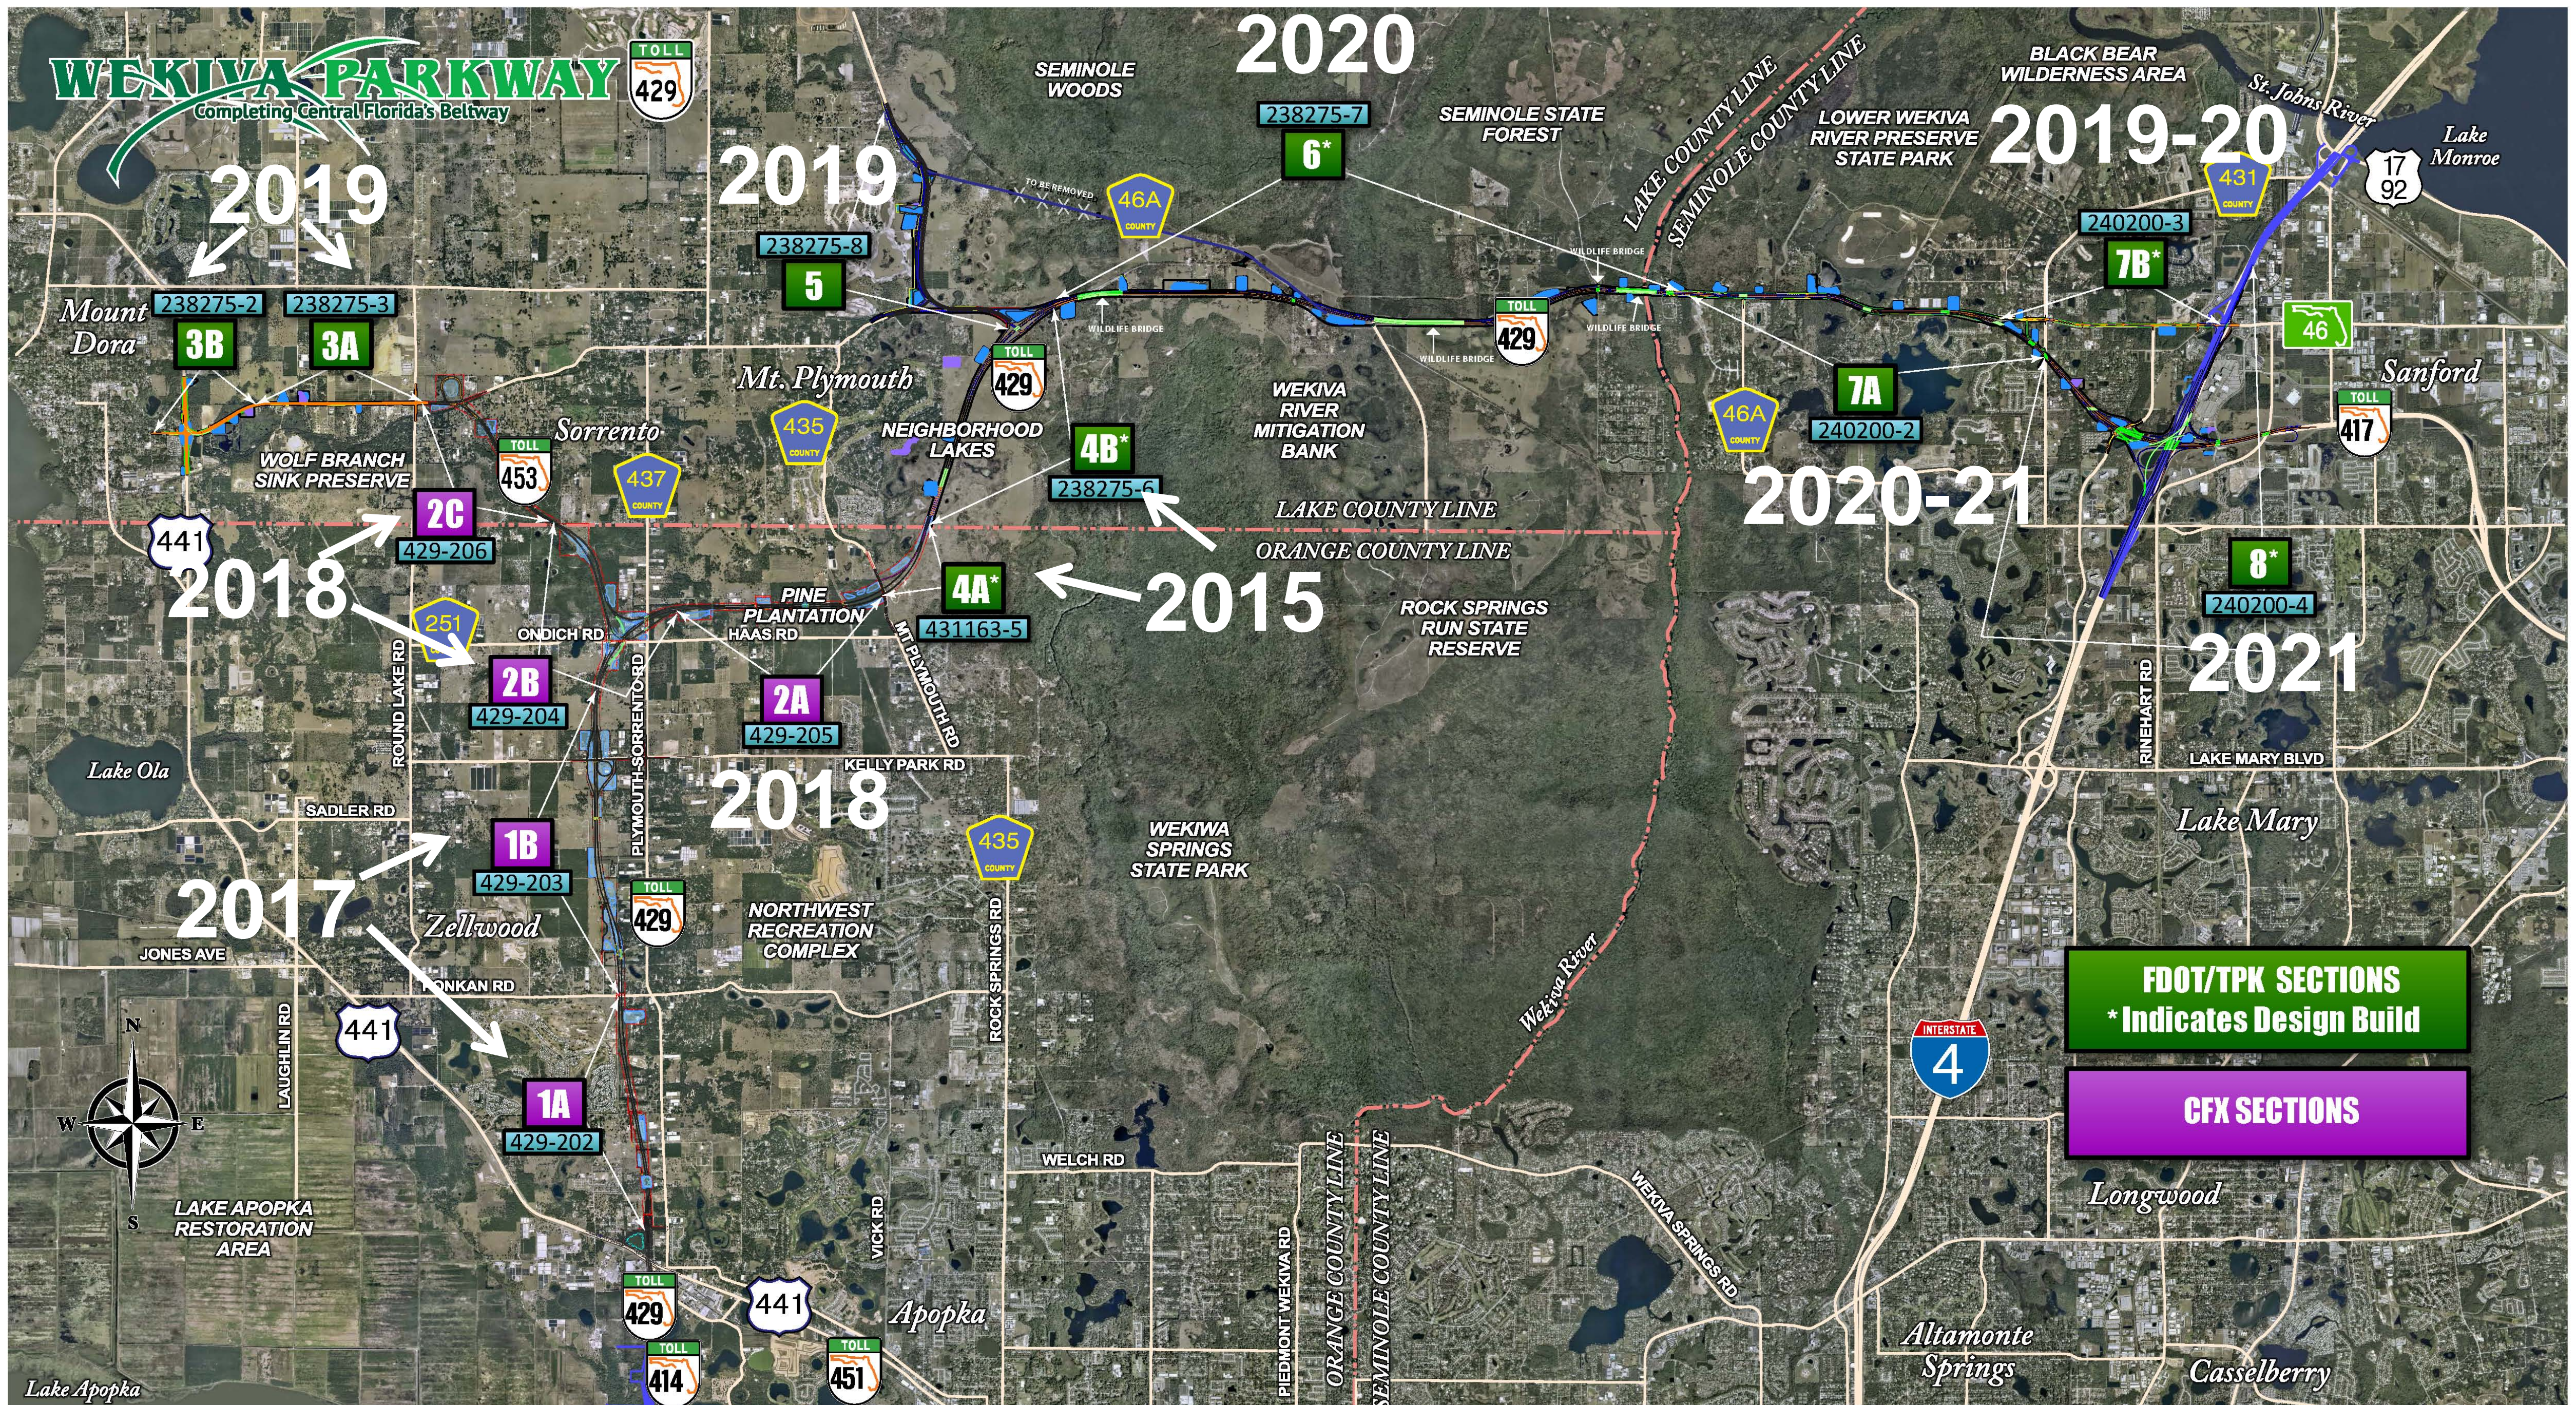



Thank You!

Questions?



CENTRAL
FLORIDA
EXPRESSWAY
AUTHORITY
