


CENTRAL FLORIDA EXPRESSWAY AUTHORITY


WEKIVA PARKWAY CONSTRUCTION
Update

WEKIVA PARKWAY

5 projects under construction

- 10 miles
- ~465 construction workers on the project on any given day
- \$271.6 million under contract
- \$150.4 million earned thru 1/25/17
- 55% complete

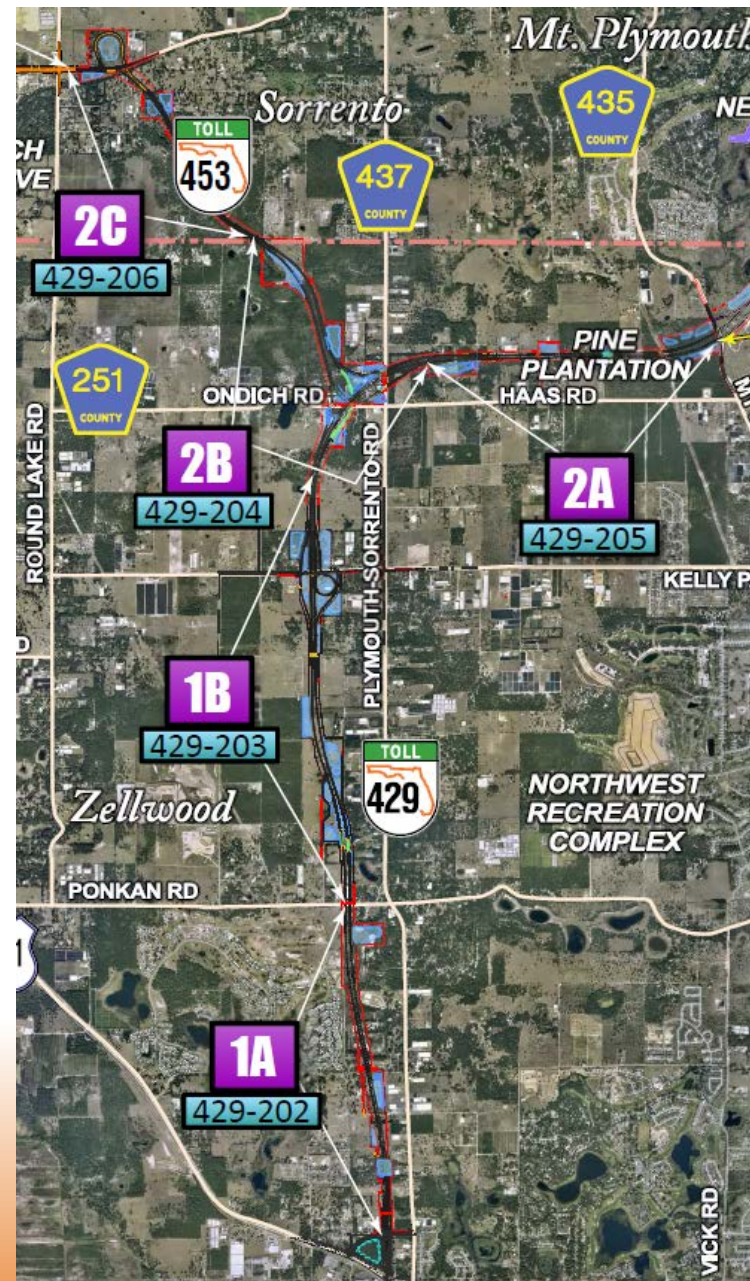



WEKIVA PARKWAY OPENING PLAN

- Mid 2017: Open Wekiva Parkway from Connector Road to Kelly Park Road [Sections 1A (429-202) & 1B (429-203)]
- Early 2018: Open remainder of CFX Wekiva Projects [Sections 2A, 2B & 2C (429-204, 429-205 & 429-206)]



Questions ?

Handouts



Section 429-202 (1A)

From North of US 441 to North of Ponkan Rd.

Started: June 8, 2015


Contractor:
Prince Construction

Contract: \$56.4 million

Earned: \$42.9 million

Time: 683 calendar days

Percent Complete: 76%

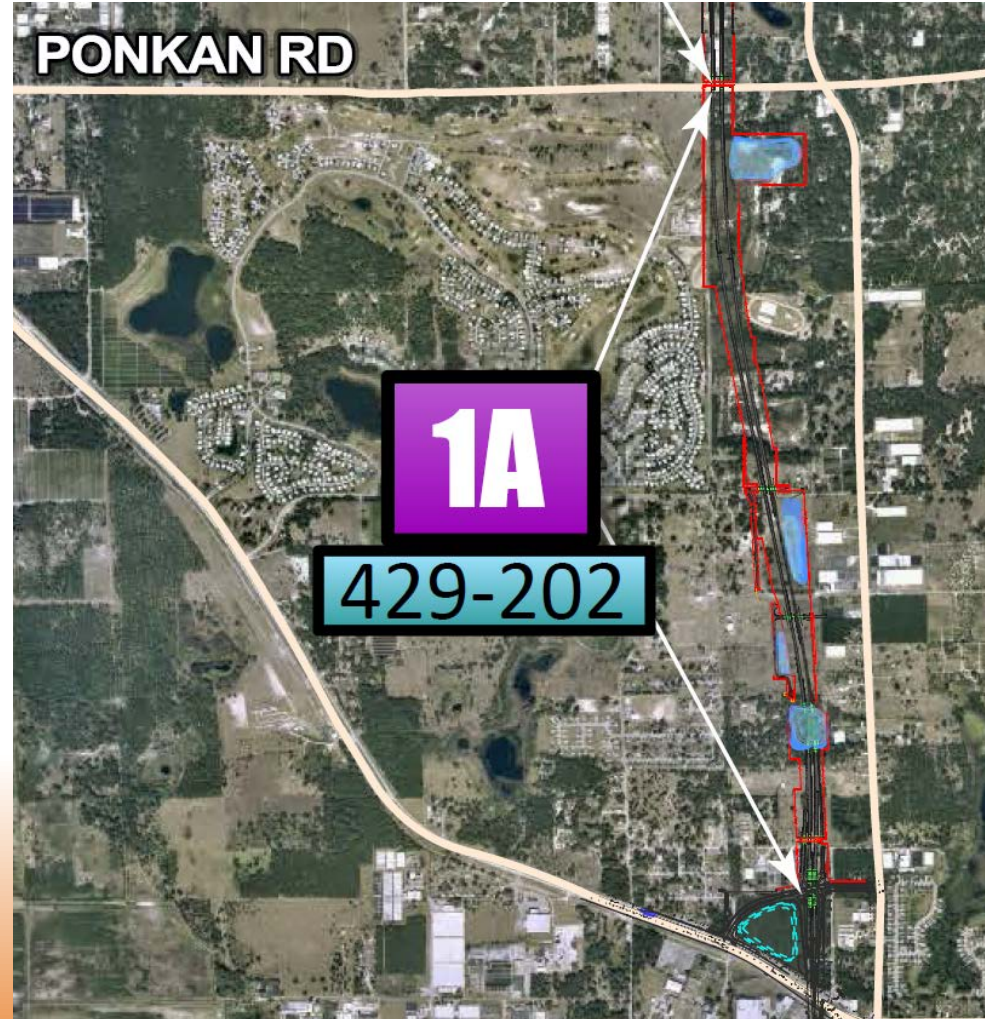



Section 429-203 (1B)

From North of Ponkan Rd. to North of a New
Kelly Park Road Interchange

Started: August 3, 2015

Contractor:

Superior Construction

Contract: \$46.6 million

Earned: \$40.9 million

Time: 600 calendar days

Percent Complete: 88%





Section 429-204 (2B)

*Systems Interchange extending Wekiva Parkway (SR 429)
northeast toward Sanford and SR 453 toward Mount Dora*

Started: January 4, 2016

Contractor:


Southland Construction

Contract: \$80.7 million

Earned: \$39.0 million

Time: 730 calendar days

Percent Complete: 48%

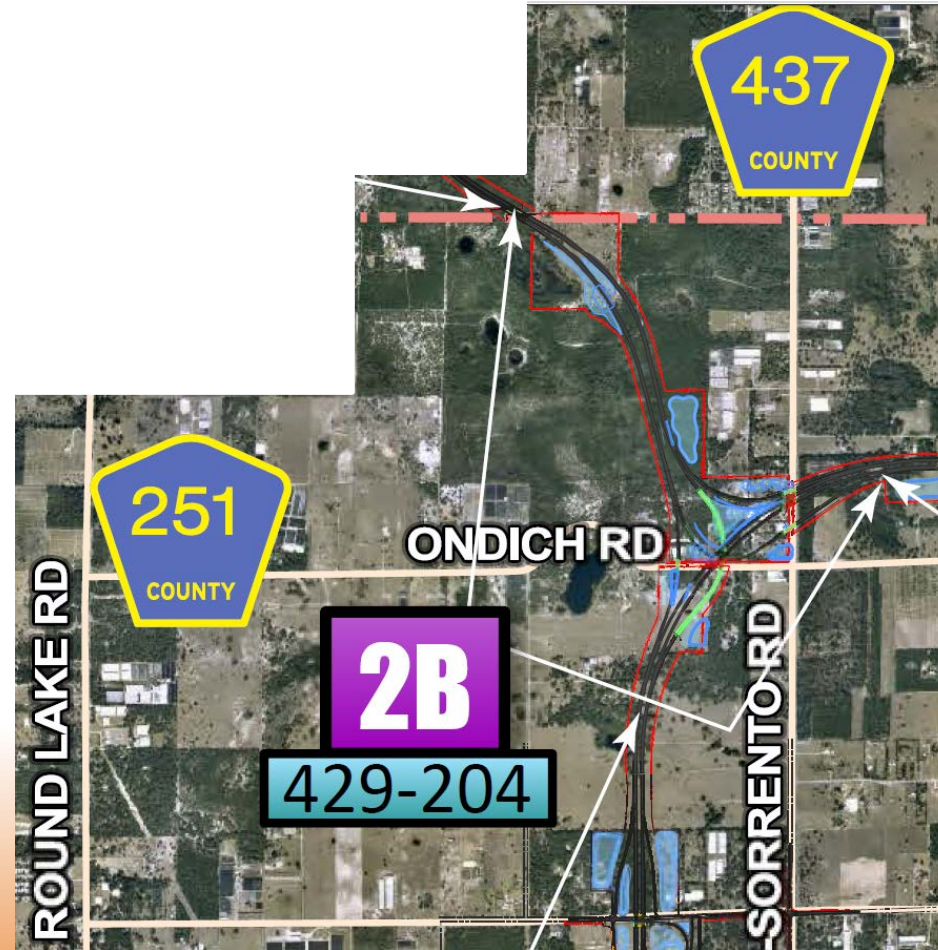



Section 429-205 (2A)

Wekiva Parkway (SR 429) from the Systems Interchange east to FDOT's completed Section 4A at CR 435

Started: August 1, 2016

Contractor:

Superior Construction


Contract: \$38.6 million

Earned: \$7.4 million

Time: 570 calendar days

Percent Complete: 19%





Section 429-206 (2C)

North-West leg of the Wekiva Parkway (SR 453) extending from the Lake County Line to SR 46 toward Mount Dora

Started: May 2, 2016


Contractor: GLF Construction

Contract: \$49.2 million

Earned: \$20.1 million


Time: 600 calendar days

Percent Complete: 41%

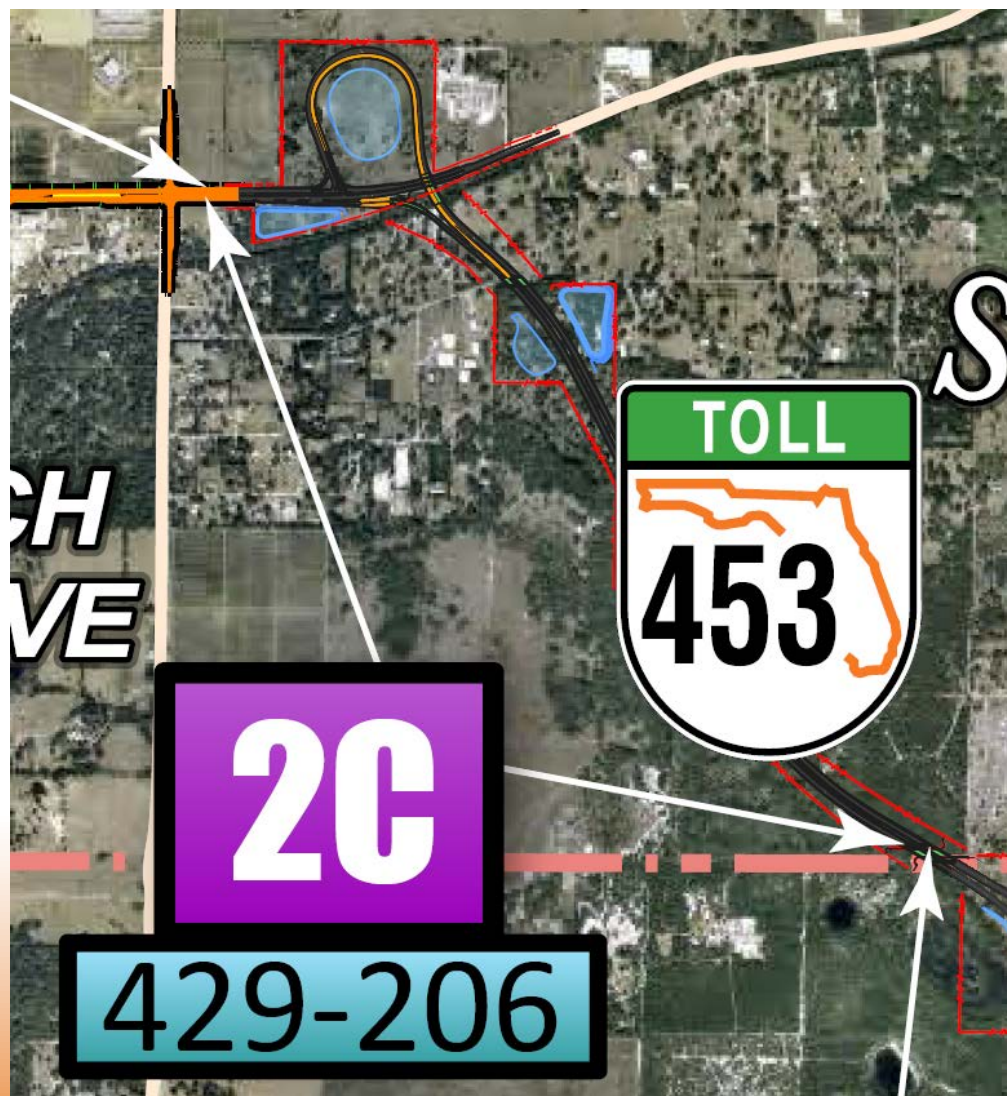

When Complete, we will have:

- Excavated ~3.6 million Cubic Yards of Earth (18 Large Cruise Ships)
- Built ~8.4 million Cubic Yards of Embankment (42 Large Cruise Ships)
- Built ~58 Lane Miles of New Expressway
- Driven ~ 40 Miles of Foundation Piles
- Built 40 New Bridges
- Planted ~ 440,000 Square Yards of Seed & Mulch (83 Football Fields)
- Placed ~ 2.3 million Square Yards of Sod (428 Football Fields)



WEKIVA PARKWAY CCEI & COMPLIANCE TEAMS

- 429-202: **RK&K**, CDM Smith, RS&H, PICS (DBE), PSI, URS, Terracon, Elipsis (DBE) AMEC, Mehta (DBE)
- 429-203: **GAI**, DRMP, PI Consulting (DBE), Page One, Ardaman, FGE, GPI, Mehta (DBE)
- 429-204: **A2** (DBE), Figg, RK&K, DRMP, GCI (DBE), Mehta (DBE), Gannett Fleming & Page One (DBE)
- 429-205: **KCCS**, Elipsis (DBE), GRL, PICS (DBE), Page One (DBE) & Echezabal (DBE)
- 429-206: **Jacobs**, Metric, FGE, Aerial Innovations, Ardaman, Elipsis (DBE) & Mehta (DBE)
- Corridor Consultant: **CH2M**
- Corridor-Wide Compliance: **MTN Resources**
