
# CENTRAL **PERFORMANCE DASHBOARD**

**SEPTEMBER 2019** Fiscal year runs from July 1-June 30

**EXPRESSWAY** 

AUTHORITY


#### **CUSTOMER SERVICE**



### WRONG WAY DRIVING (WWD)

FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP
12	14	10	16	14	14	20	14
10	10	10	15	13	14	18	13
	12	12 14	12 14 10	12 14 10 16	12 14 10 16 14	12 14 10 16 14 14	12 14 10 16 14 14 20

#### **RELOAD CUSTOMER SERVICE LANE ACTIVITY**

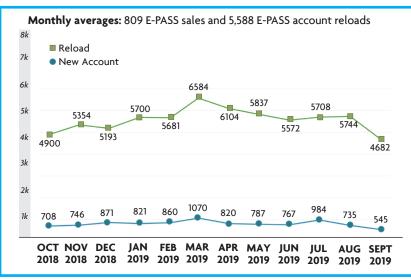

## PROGRESS OF MAJOR CONSTRUCTION PROJECTS

	Contract (millions)	Spent (millions)	% Time	% Spent	VAR	Contract Completion Date
SR 408/SR 417 Interchange (Phase II)	\$66.8	\$61.2	92%	92%		January 2020
SR 408 Widening from SR 417 to Alafaya Trail	\$78.4	\$73.6	95%	94%		November 2019
SR 417 Widening from Econlockhatchee to Seminole Co.	\$44.4	\$29.7	63%	67%		June 2020
Toll System Replacement	\$54.4	\$30.8	70%	57%		July 2021
LEGEND: % Time - % Spent ≤ 10 11-20 22	21					

#### **FINANCIALS**

